

Fire Hydrant Flow Test Form



Test form to be filled out and returned in PDF format.

Click to **Reset Fields** in II. Flow Test Data and III. Calculations.

Hover cursor over fields to display ToolTips.

I. Project Information (To be completed by Applicant)		
Name:	V.K. Knowlton Construction & Utilities, Inc.	Phone: (210) 651-6860
Company Address:	18225 FM 2252, San Antonio, Texas 78266	
Project Name:	VERAMENDI PRECINCT 18, UNIT 1	
NBU Work Order Numbers:	W-226995 / WW-226996	

TEST #25

II. Flow Test Data (To be completed by Applicant)			
Test Hydrant	NBU FH ID #: 1 F/H	Plan Sheet/Hydrant #: Exhibit - 1 F/H	Private: No
	Location Description: Pennyroyal Lane / Hill Country Drive		
	Size and Material of Main: 16" main C-900 PVC (200)		
	Manufacturer: CLOW		OEM Year: 2025
	Static PSI: 52	Residual PSI: 42	% Pressure Drop: 19.23 Date and Time: 5/15/2026 12:13 pm
Flow Hydrant	NBU FH ID #: 14 F/H	Plan Sheet/Hydrant #: Exhibit - 14 F/H	Diameter: 2.5
	Size and Material of Main: 12" main C-900 PVC (200)		
	Pitot PSI: 35	Observed Flow (GPM): 993	Mins Flowed: 1 Date and Time: 5/15/2026 12:13 pm
	Total Water Loss: 993		
Flow Hydrant	NBU FH ID #: 14 F/H	Plan Sheet/Hydrant #: Exhibit - 14 F/H	Diameter: 2.5
	Size and Material of Main: 12" main C-900 PVC (200)		
	Pitot PSI: 35	Observed Flow (GPM): 993	Mins Flowed: 1 Date and Time: 5/15/2026 12:13 pm
	Total Water Loss: 993		

III. Calculations (Auto-populated)	
Residual Flow $Q_r = 29.83 \times c_d \times D^2 \sqrt{P_p \times H_f}$	Fire Flow at 20 PSI $Q_f = Q_r \times ((P_s - 20) / (P_s - P_r))^{0.54}$
Cd = 0.9	Qr = 1985
D = 2.5	Ps = 52
Pp = 35	Pr = 42
Hf = 2	Qf = 3721
Qr = 1985	NFPA 291 Standard Color Code : 1500 GPM & Above = Light Blue


IV. Tester/Company Information (To be completed by Applicant)	
Flow Test Conducted by: Protection Development, Incorporated	Phone: (210) 828-7533
Business License #: Texas Registered Engineering Firm (F-2816)	
Company Address: 8620 N. New Braunfels Avenue, Suite 100, San Antonio, Texas 78217	
Signature: Geoff Owens & Alex Akeroyd <i>[Handwritten Signature]</i>	Date: 05/15/2026

V. NBFDD Fire Hydrant Flow Requirements (To be completed by Fire Department)		
Print Name:	Title:	Accepted: <input type="checkbox"/>
Signature:	Date and Time:	





Project Name:	Veramendi Pct 18, Unit 1 - Test #25
Project Number:	26-0064
Test Date:	May 15, 2026
City:	New Braunfels

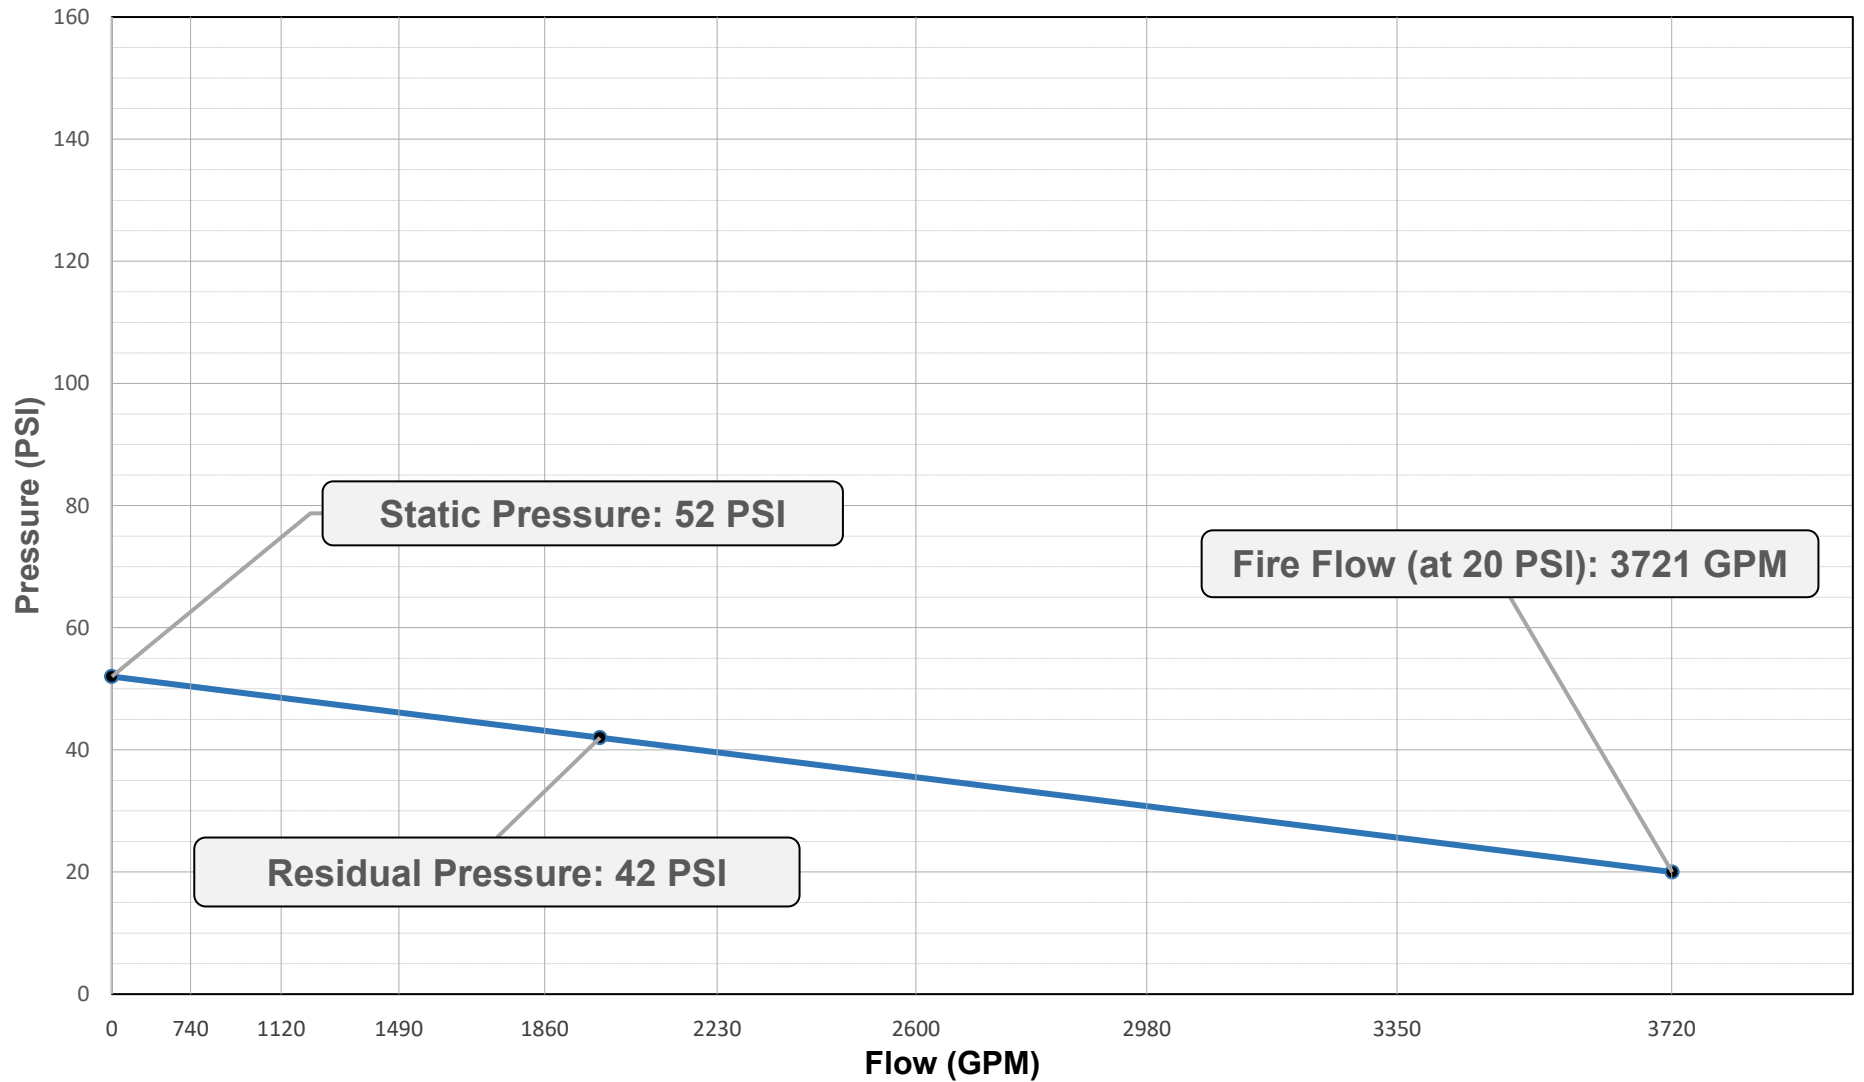

Static Pressure: 52 PSI	Residual Pressure: 42 PSI	Flow Test @ Residual Pressure: 1,985 GPM	Fire Flow (at 20 PSI): 3,721 GPM
--------------------------------	----------------------------------	---	---
