



Oldcastle
Infrastructure
A CRH COMPANY

1900 Rilling Road
San Antonio, TX 78214
210-923-4523
N/A

Job Name: Agave Unit 2

Quote ID: S038597

Date Printed:

4/22/2024

Contractor: V. K. KNOWLTON PAVING

Salesperson: PaulVarga

Delivery Date: N/A

Item Code	Description	Ref	Qty	Weight
7040004	MH Boot - PSX ND 11-06 - Nylo Drive		2	0
7040008	MH Boot - PSX ND 11-08 Nylo Drive		2	0
7045011	48" Dia. Gasket-Non-Lubed (HK: 822467)		3	0
1015050	Sanitary Manhole Invert 48"		1	1809
7011022	ERGO 30 DI CAM SAWS SS LO ASY 4.5	G	1	293
1012413	Grade Ring 34"x2"	F	1	0
1012413	Grade Ring 34"x2"	E	1	0
1015082	48 Dia x 24 Cone w/35" OP CONC (Q7R Joint)	D	1	2390
1015019	48 Dia x 18 Riser (Q7R Joint)	C	1	1394
1015033	48 Dia x 36 Riser (Q7R Joint)	B	1	2557
1014006	48 Dia x 36" Yield Base (6F) MS	A	1	3745
Structure Total				10379

Structure ID: MH A3

Station: 5+61.51

Type: Sanitary

Size: 48" Dia SAWS Sanitary MH

Rim: 562.5'

Lowest Invert: 552.27'

Design Height: 10'-2³/₄"


Overall Height: 10'-10¹/₄"

Slack: 1³/₄"

Steps: D0/0

N/A

Handwritten signature: Jm 4/22

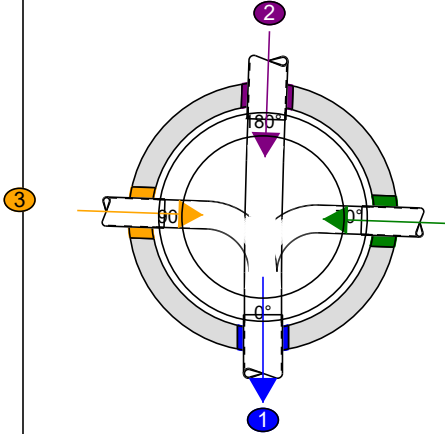

#	Elev	Angle	Ext (cw)	Hole	Pipe	Upt	Connector
1	552.27	0	0	11	8 PVC SDR 26/3	0	MH Boot - PSX ND 11-08 Nylo Driv
2	552.37	182	92.011	11	8 PVC SDR 26/3	1	MH Boot - PSX ND 11-08 Nylo Driv
3	553.82	92	46.511	11	6 PVC SDR 26/3	17	MH Boot - PSX ND 11-06 - Nylo Dri
4	553.82	272	137.511	11	6 PVC SDR 26/3	17	MH Boot - PSX ND 11-06 - Nylo Dri

Shop Note: Concrete strength of 2,000 psi minimum must be obtained for stripping/lifting structure

