



Oldcastle 1900 Rilling Road
Infrastructure, San Antonio, TX 78214
A CRH COMPANY 210-923-4523
N/A

Job Name: Agave Unit 2

Quote ID: S038597

Date Printed:

4/22/2024

Contractor: V. K. KNOWLTON PAVING

Salesperson: PaulVarga

Delivery Date: N/A

Item Code	Description	Ref	Qty	Weight
7040008	MH Boot - PSX ND 11-08 Nylo Drive		3	0
7045011	48" Dia. Gasket-Non-Lubed (HK: 822467)		2	0
1015050	Sanitary Manhole Invert 48"		1	1809
7011022	ERGO 30 DI CAM SAWS SS LO ASY 4.5	G	1	293
1012413	Grade Ring 34"x2"	F	1	0
1012413	Grade Ring 34"x2"	E	1	0
1012413	Grade Ring 34"x2"	D	1	0
1015082	48 Dia x 24 Cone w/35" OP CONC (Q7R Joint)	C	1	2390
1015035	48 Dia x 48 Riser (Q7R Joint)	B	1	3413
1014003	48 Dia x 30" Yield Base (6F) MS	A	1	3525
Structure Total				9621

Structure ID: MH A5

Station: 12+51.58

Type: Sanitary

Size: 48" Dia SAWS Sanitary MH

Rim: 585.4'

Lowest Invert: 576.41'

Design Height: 9'-3"

Overall Height: 9'-10½"


Slack: "

Steps: D0/0

N/A

DM 4/22

#	Elev	Angle	Ext (cw)	Hole	Pipe	Upt	Connector
1	576.38	0	0	11	8 PVC SDR 26/3	3	MH Boot - PSX ND 11-08 Nylo Driv
2	576.14	90	45.5	11	8 PVC SDR 26/3	0	MH Boot - PSX ND 11-08 Nylo Driv
3	576.41	270	136.5	11	8 PVC SDR 26/3	3	MH Boot - PSX ND 11-08 Nylo Driv

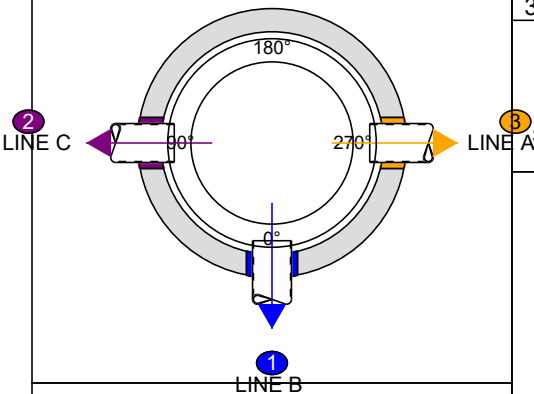

Shop Note: Concrete strength of 2,000 psi minimum must be obtained for stripping/lifting structure

