




1900 Rilling Road
San Antonio, TX 78214
210-923-4523
N/A

Job Name: Agave Unit 2
Quote ID: S038597

Contractor: V. K. KNOWLTON PAVING
Salesperson: PaulVarga
Delivery Date: N/A

Date Printed:
4/22/2024

Item Code	Description	Ref	Qty	Weight	Structure ID: MH B2 Station: 6+84.14 Type: Sanitary Size: 48`` Dia SAWS Sanitary MH Rim: 560.3' Lowest Invert: 552.18' Design Height: 8'-1½" Overall Height: 8'-9" Slack: 4½"Steps: D0/0
7040004	MH Boot - PSX ND 11-06 - Nylo Drive		1	0	
7040008	MH Boot - PSX ND 11-08 Nylo Drive		2	0	
7045011	48" Dia. Gasket-Non-Lubed (HK: 822467)		2	0	
1015050	Sanitary Manhole Invert 48"		1	1809	
7011022	ERGO 30 DI CAM SAWS SS LO ASY 4.5	G	1	293	
1012413	Grade Ring 34``x2``	F	1	0	
1012413	Grade Ring 34``x2``	E	1	0	
1012413	Grade Ring 34``x2``	D	1	0	
1015082	48 Dia x 24 Cone w/35`` OP CONC (Q7R Joint)	C	1	2390	N/A
1015033	48 Dia x 36 Riser (Q7R Joint)	B	1	2557	
1014002	48 Dia x 24`` Yield Base (6F) MS	A	1	3082	
Structure Total				8322	

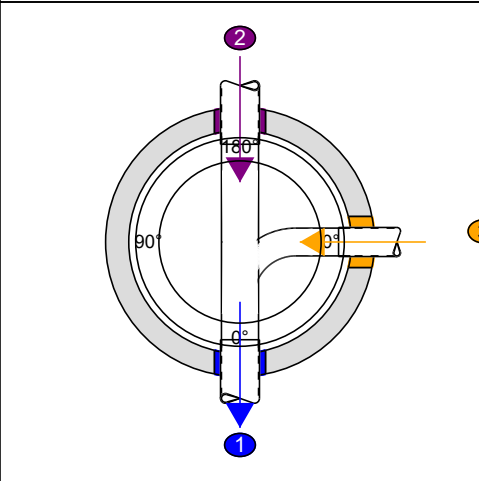

#	Elev	Angle	Ext (cw)	Hole	Pipe	Upt	Connector
1	552.18	0	0	11	8 PVC SDR 26/3	0	MH Boot - PSX ND 11-08 Nylo Driv
2	552.28	180	91	11	8 PVC SDR 26/3	1	MH Boot - PSX ND 11-08 Nylo Driv
3	552.32	270	136.5	11	6 PVC SDR 26/3	0.5	MH Boot - PSX ND 11-06 - Nylo Dri

Shop Note: Concrete strength of 2,000 psi minimum must be obtained for stripping/lifting structure

