



Oldcastle 1900 Rilling Road
Infrastructure, San Antonio, TX 78214
A CRH COMPANY 210-923-4523
N/A

Job Name: Agave Unit 2

Quote ID: S038597

Date Printed:

4/22/2024

Contractor: V. K. KNOWLTON PAVING

Salesperson: PaulVarga

Delivery Date: N/A

Item Code	Description	Ref	Qty	Weight
7040008	MH Boot - PSX ND 11-08 Nylo Drive		1	0
7045011	48" Dia. Gasket-Non-Lubed (HK: 822467)		3	0
7011022	ERGO 30 DI CAM SAWS SS LO ASY 4.5	G	1	293
1012413	Grade Ring 34"x2"	F	1	0
1012413	Grade Ring 34"x2"	E	1	0
1015082	48 Dia x 24 Cone w/35" OP CONC (Q7R Joint)	D	1	2390
1015020	48 Dia x 12 Riser (Q7R Joint)	C	1	1215
1015033	48 Dia x 36 Riser (Q7R Joint)	B	1	2557
1014553	48 Dia x 24" Yield Base w/Invert (0) (Q7R Joint) S	A	1	4471
Structure Total				10926

Structure ID: MH E1

Station: 3+90.00

Type: Sanitary

Size: 48" Dia SAWS Sanitary MH

Rim: 583.1'

Lowest Invert: 574.36'

Design Height: 8'-9"

Overall Height: 9'-4½"


Slack: 2"

Steps: D0/0

N/A

DM 4/22

#	Elev	Angle	Ext (cw)	Hole	Pipe	Upt	Connector
1	574.36	0	0	11	8 PVC SDR 26/3	0	MH Boot - PSX ND 11-08 Nylo Driv

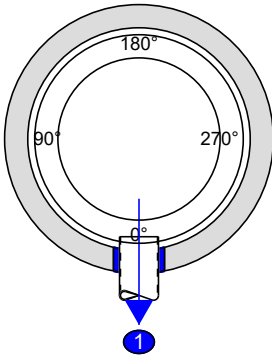

Shop Note: Concrete strength of 2,000 psi minimum must be obtained for stripping/lifting structure

