

Fire Hydrant Flow Test Form

Required fields highlighted in blue.

Auto-populated Fields:

% Pressure Drop, Total Water Loss, Residual Flow, Fire Flow at 20PSI, and NFPA 291 Standard Color Code.

I. Project Information						
Name: V.K. Knowlton Construction & Utilities, Inc.				Phone: (210) 651-6860		
Company Address: 18225 FM 2282 San Antonio, TX 78266						
Project Name: THE LANDING - UNIT 1						
NBU Work Order Numbers:						

Point #	Grid Easting	Grid Northing	Elevation	Code	FH#	
23	13812561.4000	2273482.2640	673.443	F/H	12	12

II. Flow Test Data						
Click Reset Fields to recalculate auto-populated fields.						
Test Hydrant	NBU FH ID #:		Plan Sheet/Hydrant #: Sheet C6.1		11	Private: No
	Location Description: Climb Ridge at Cargo Trails					
	Size and Material of Main: 8 inch main C-900 (200)					
	Manufacturer: CLOW			OEM Year: 2023		
	Static PSI: 99	Residual PSI: 58	% Pressure Drop: 41.41	Date and Time: 2/13/2025 10:35 am		
Flow Hydrant 1	NBU FH ID #:		Plan Sheet/Hydrant #: Sheet C6.0		12	Diameter: 2.5
	Size and Material of Main: 8 inch main C-900 (200)					
	Pitot PSI: 26	Observed Flow:	856	Minutes Flowed: 2		
	Total Water Loss: 1712					
Flow Hydrant 2 (OPTIONAL)	NBU FH ID #:		Plan Sheet/Hydrant #: Sheet C6.0		12	Diameter: 2.5
	Size and Material of Main: ~~FLOWING BOTH OUTLETS OF HYDRANT 1~~					
	Pitot PSI: 26	Observed Flow:	856	Minutes Flowed: 2		
	Total Water Loss: 1712					

III. Calculations (Auto-populated)	
Residual Flow $Q_r = 29.83 \times c_d \times D^2 \sqrt{P_p \times H_f}$	Fire Flow at 20 PSI $Q_f = Q_r \times ((P_s - 20) / (P_s - P_r))^{0.54}$
Cd = 0.9	Qr = 1711
D = 2.5	Ps = 99
Pp = 26	Pr = 58
Hf = 2	Qf = 2438
Qr = 1711	NFPA 291 Standard Color Code : 1500 GPM & Above = Light Blue


IV. Tester/Company Information	
Flow Test Conducted by: PROTECTION DEVELOPMENT, INCORPORATED	Phone: (210) 828-7533
Business License #: Texas Registered Engineering Firm (F-2816)	
Company Address: 8620 North New Braunfels Avenue, Suite 100, San Antonio, Texas 78217	
Print Name: Alex Akeroyd and Nicholas Balanciere	Date: 02/13/2025

V. NBFD Fire Hydrant Flow Requirements (To be completed by Fire Department)		
Print Name:	Title:	Accepted: <input type="checkbox"/>
Signature:	Date and Time:	


Fire Hydrant Flow Test Form

VI. Sketch (Attach any additional calculations and graphs made by testing company)

Label Hydrant Numbers and Street Names

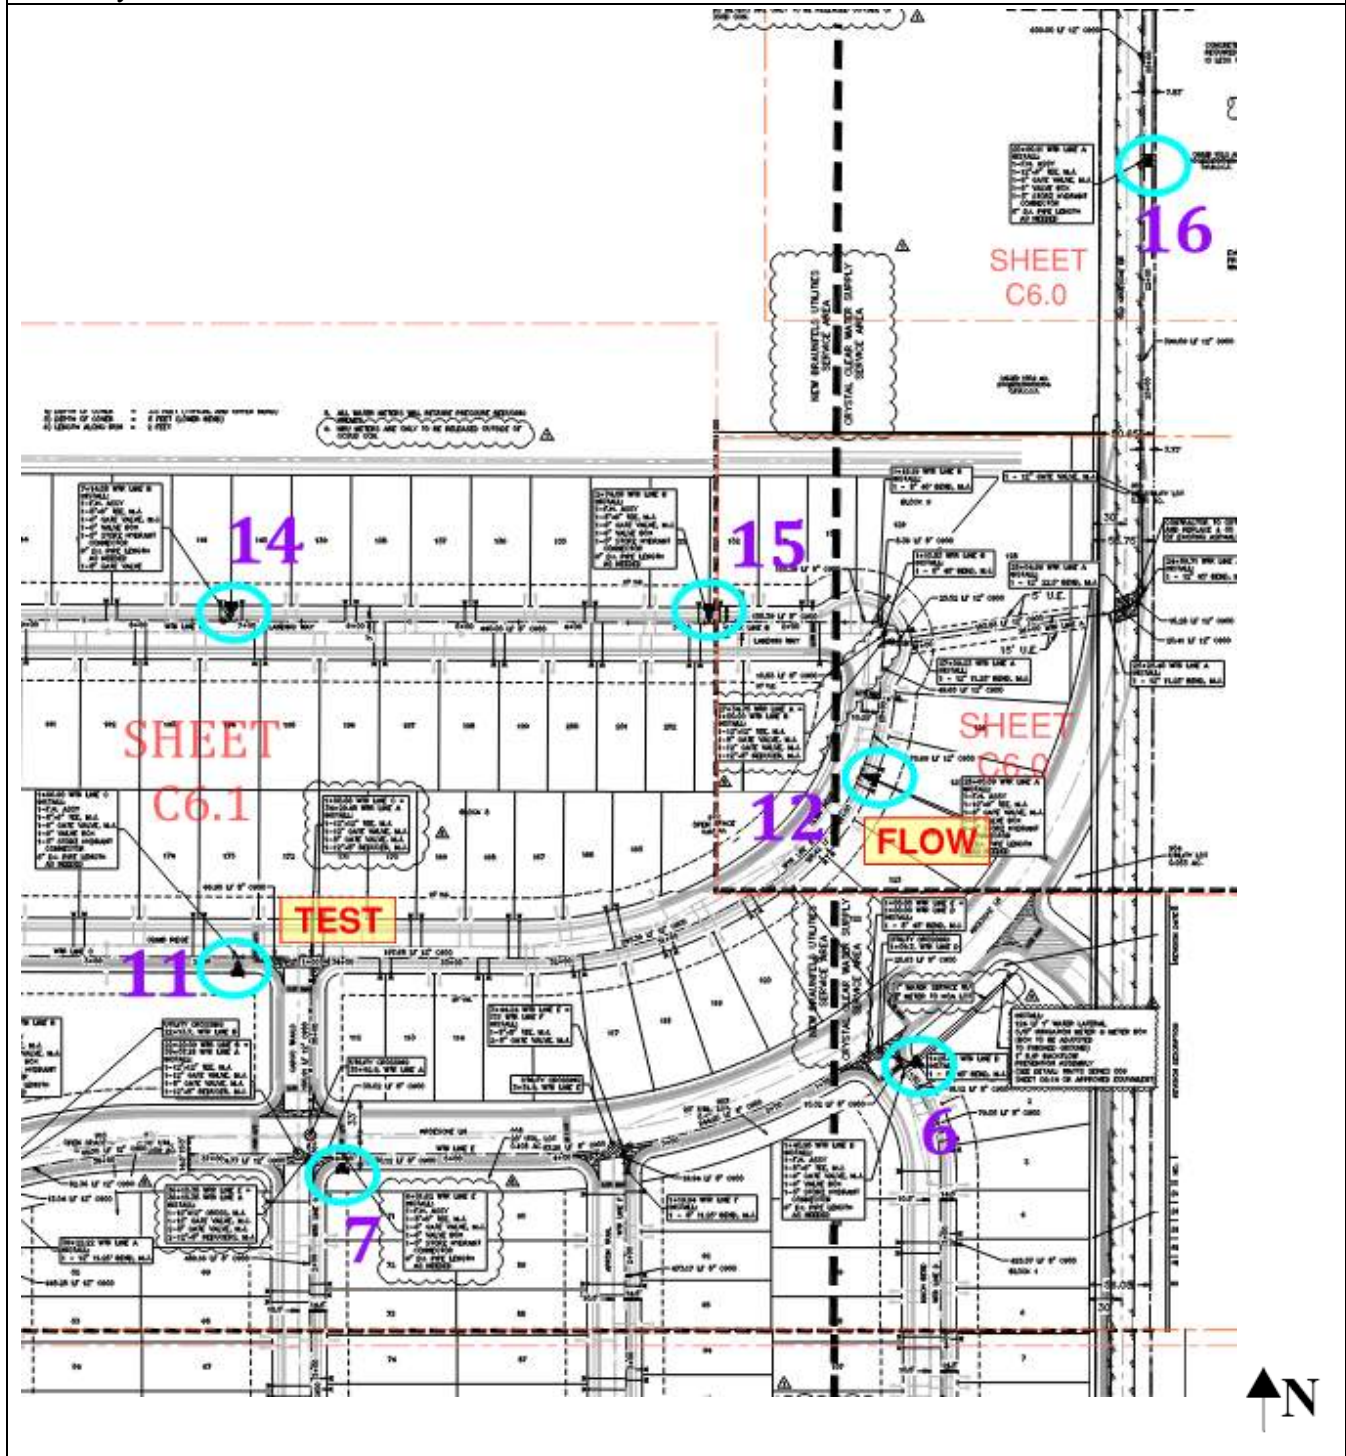

Project Name:	The Landing Unit 1 - Test #12
Project Number:	25-0033
Test Date:	February 13, 2025
City:	New Braunfels

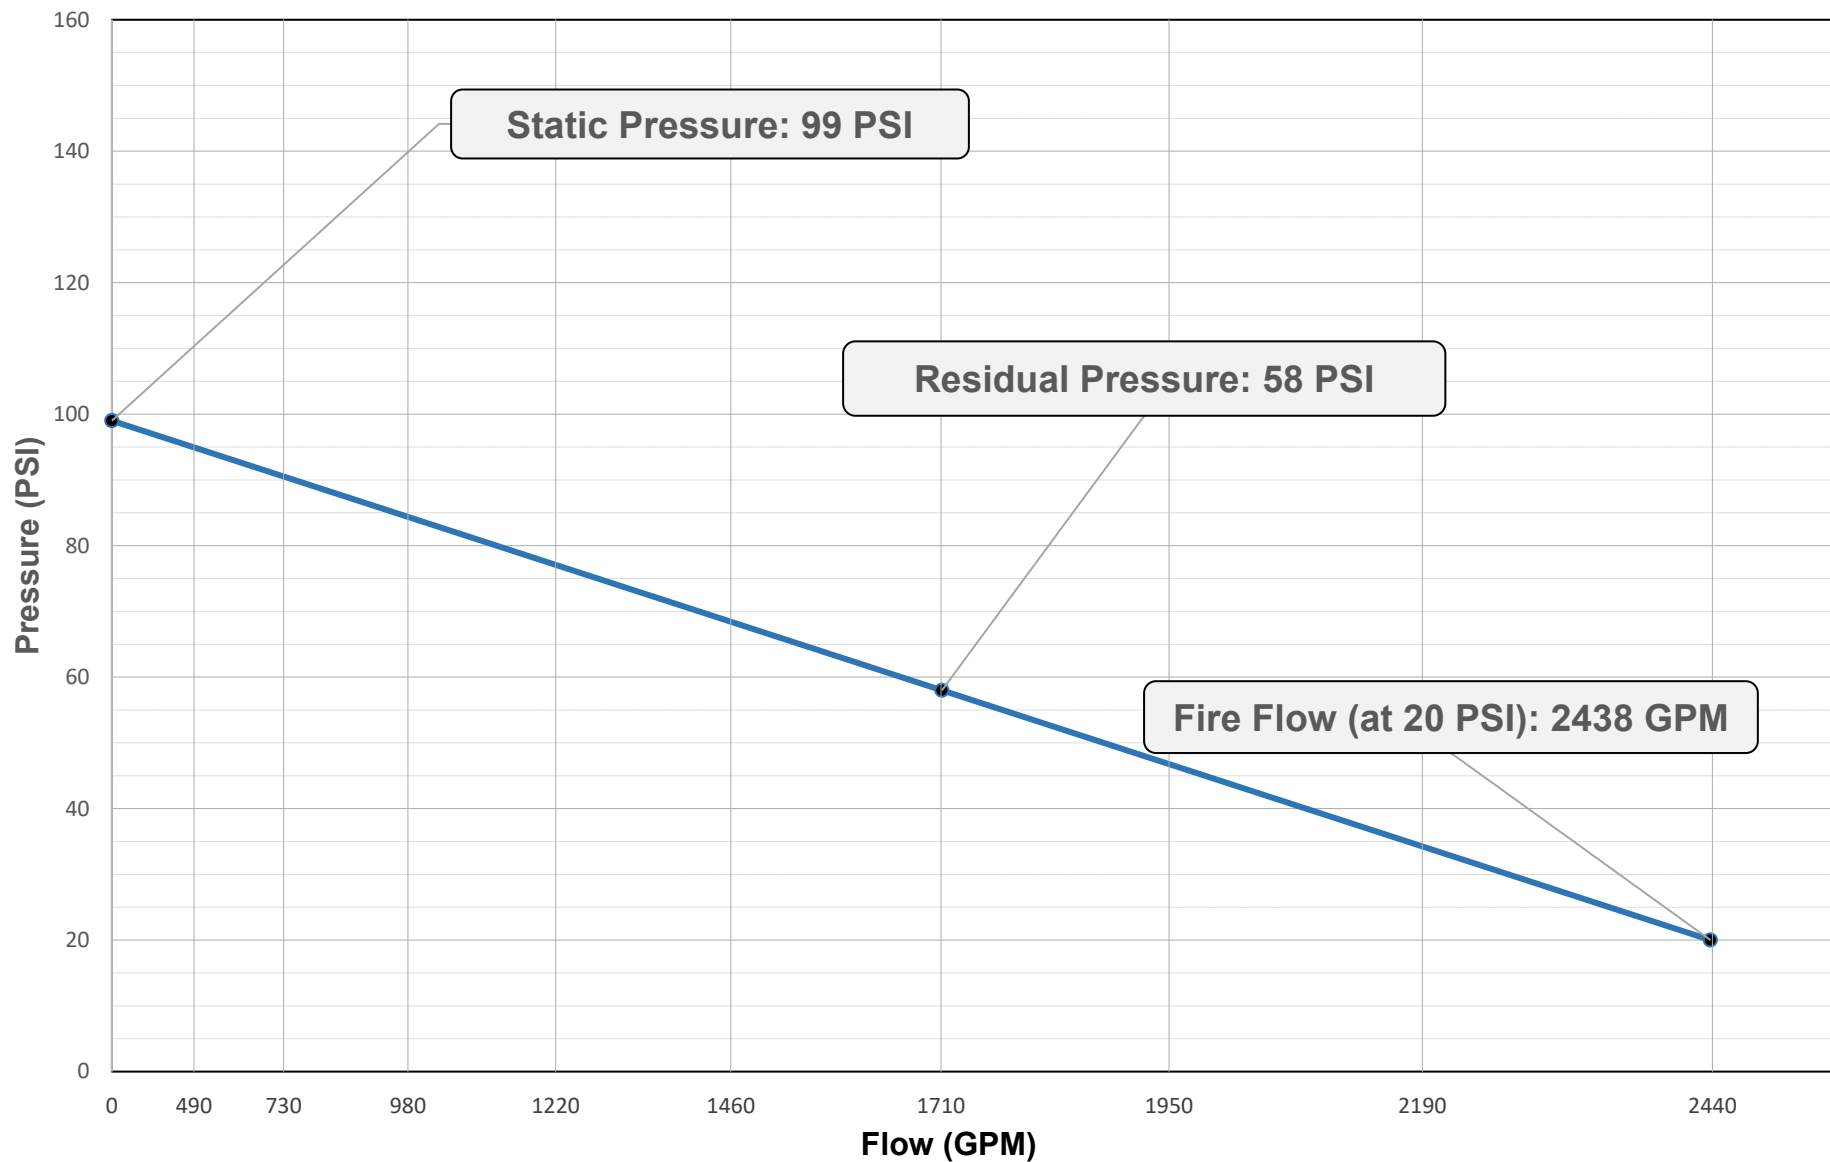

Static Pressure: 99 PSI	Residual Pressure: 58 PSI	Flow Test @ Residual Pressure: 1,711 GPM	Fire Flow (at 20 PSI): 2,438 GPM
-------------------------	---------------------------	--	----------------------------------
